

**Curve Data**  
 N • KC10013  
 • • 61°54'22" (RT)  
 D • 11'20'58"  
 T • 302.78  
 L • 545.46  
 E • 83.83  
 R • 504.84  
 C • 519.31  
 CB • N 73°35'00" E  
 DB • N 42°37'49" E  
 DA • S 75°27'49" E  
 SE • 8%

**WHITE RD RELOCATION  
 CURVE KC10013  
 SE TABLE**

Station	Type
94+21.29	End FS
94+71.53	Sh. Trans.
95+22.85	Rev. Crown
95+57.07	Zero Super
95+91.29	Begin NC


**SR108  
 CURVE SVA10  
 SE TABLE**

Station	Type
52+30.05	Sh End NC
52+91.22	End NC
53+32.01	Zero Super
53+72.80	Rev. Crown
54+33.97	Sh. Trans.
54+94.84	Begin FS
58+37.00	PI
61+42.99	End FS
62+03.86	Sh. Trans.
62+65.03	Rev. Crown
63+05.82	Zero Super
63+46.61	Begin NC
64+07.78	Sh Begin NC

**Curve Data**  
 N • KC10011  
 • • 13°23'32" (LT)  
 D • 10'07'39"  
 T • 66.42  
 L • 132.24  
 E • 3.89  
 R • 565.75  
 C • 131.94  
 CB • S 84°56'60" E  
 DB • S 78°15'14" E  
 DA • N 88°21'14" E  
 SE • 5%

**Curve Data**  
 N • KC10014  
 • • 42°21'17" (LT)  
 D • 29'07'58"  
 T • 76.19  
 L • 145.39  
 E • 14.24  
 R • 196.67  
 C • 142.10  
 CB • N 66°16'11" E  
 DB • N 87°26'49" E  
 DA • N 45°05'32" E  
 SE • 5%

**Curve Data**  
 N • SVA10  
 • • 42°55'58" (LT)  
 D • 5'53'04"  
 T • 382.89  
 L • 729.60  
 E • 72.58  
 R • 973.69  
 C • 712.65  
 CB • N 12°56'10" E  
 DB • N 34°24'09" E  
 DA • N 8°31'49" W  
 SE • 8%

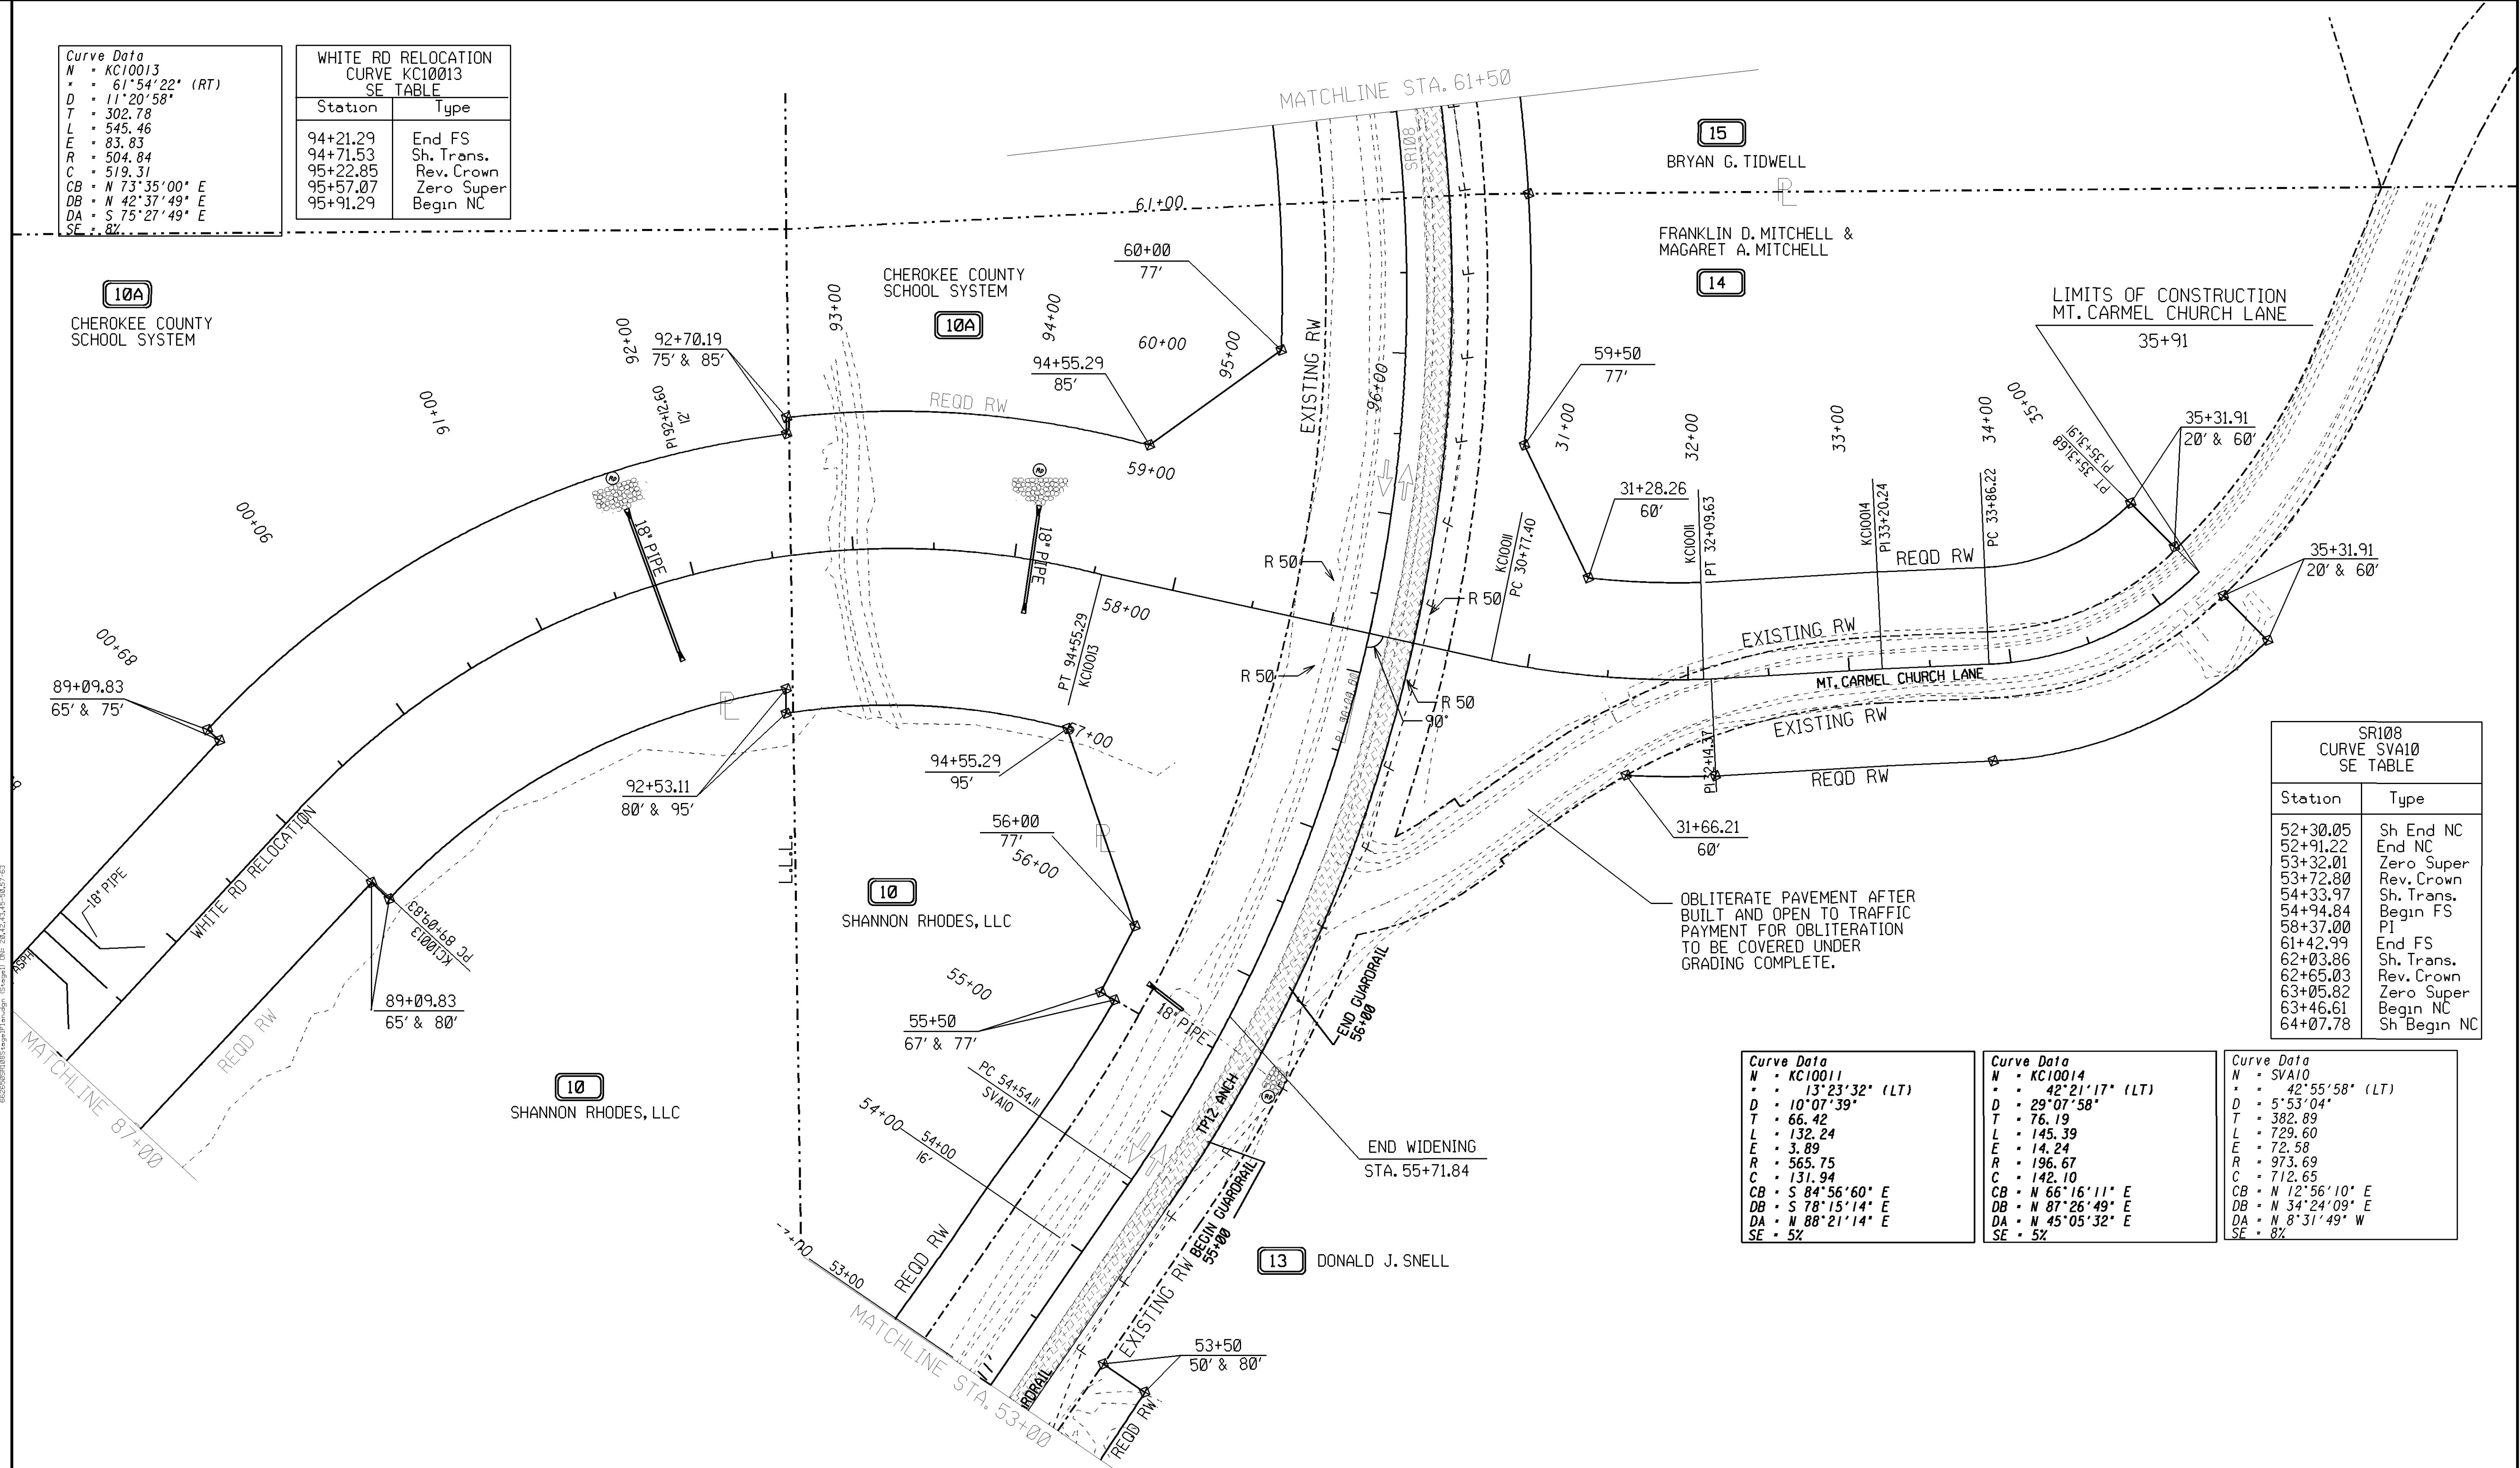

**LEGEND**

PAVEMENT REMOVAL	
TEMPORARY CONSTRUCTION PAVEMENT	
PERMANENT CONSTRUCTION	
CONCRETE MEDIAN CONSTRUCTION	
MILL & OVERLAY CONSTRUCTION	
OPEN LANES OF TRAFFIC	

**GEORGIA  
 DEPARTMENT  
 OF  
 TRANSPORTATION**



STATE OF GEORGIA  
 DEPARTMENT OF TRANSPORTATION  
 OFFICE: DISTRICT SIX ROAD DESIGN  
**CONSTRUCTION STAGING  
 PLAN**  
 SR108 STAGE 1

DRAWING No.  
**19-08**
