STATE	PROJECT NUMBER	SHEET NO.	TOTAL SHEETS
GA	NH000-0073-03(242)		

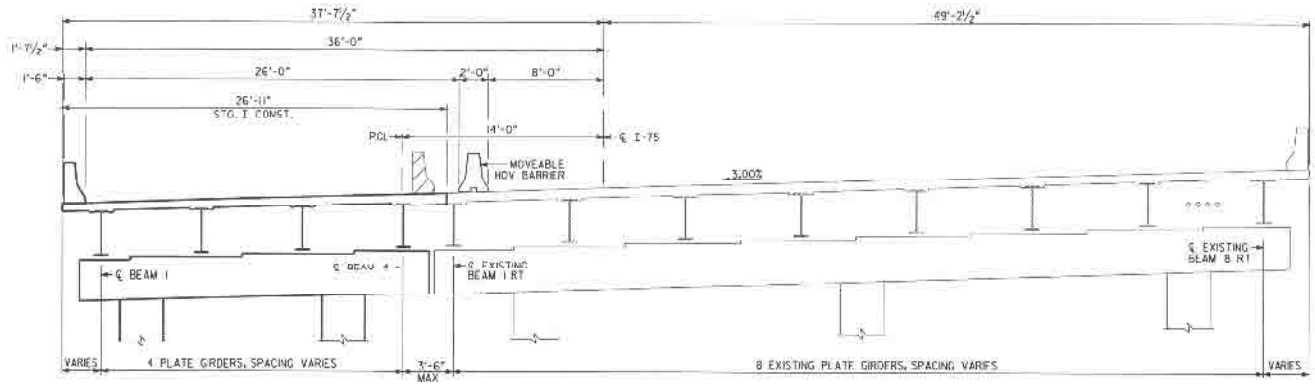

DECK SECTION
(LOOKING AHEAD, RIGHT BRIDGE)

CONSTRUCTION SEQUENCE

STAGE I:

1. PLACE TEMPORARY BARRIER, MAINTAIN THREE 12'-0" LANES OF TRAFFIC IN EACH DIRECTION ON EXISTING NB BRIDGE.
2. REMOVE PORTIONS OF EXISTING NORTH BOUND BRIDGE AS NECESSARY FOR STAGE I CONSTRUCTION.
3. CONSTRUCT STAGE I SUBSTRUCTURE.
4. CONSTRUCT STAGE I SUPERSTRUCTURE.

NOTE IF IMPORTANT NOTICE! THIS DRAWING IS AN INCOMPLETE WORK-IN-PROGRESS AND ITS USE IS SUBJECT TO NOTE 1 ON DRAWING NO. 1-01.

BRIDGE NO. 33

		REVISIONS					
NAME (PRINTED PLEASE)	1/20/05	NO	DATE	DESCRIPTION	DRG	CHK	SUPV	APPR
DRAWN BY	DATE	A	6/30/09	[illegible]	APW	CR	DLE	[illegible]
CHECKED BY	DATE	B	10/29/09	ADD SIDEWALK	APW	CR	DLE	[illegible]
		C	1/28/09	ADD TLS TO CONSTRUCTION FOR COMPLETE DIRECTION	APW			
SUPERVISOR	DATE							
APPROVED	DATE							

GTP Georgia Transportation Partners

NORTHWEST I-75/I-575 CORRIDOR

DEPARTMENT OF TRANSPORTATION
STATE OF GEORGIA

JBT J.B. Trimble, Inc.
2550 Heritage Ct. Se Suite 250
Atlanta GA 30339-3062
(770) 952-1022

BRIDGE SHEET 2 OF 8

I-75 / I-575 NORTHWEST CORRIDOR

I-75 REVERSIBLE OVER FREY RD
CONSTRUCTION SEQUENCE

COBB COUNTY NH000-0073-03(242)

DRAWING NO. 35-209
