STATE	PROJECT NUMBER	SHEET NO.	TOTAL SHEETS
GA	NH000-0073-03(242)		

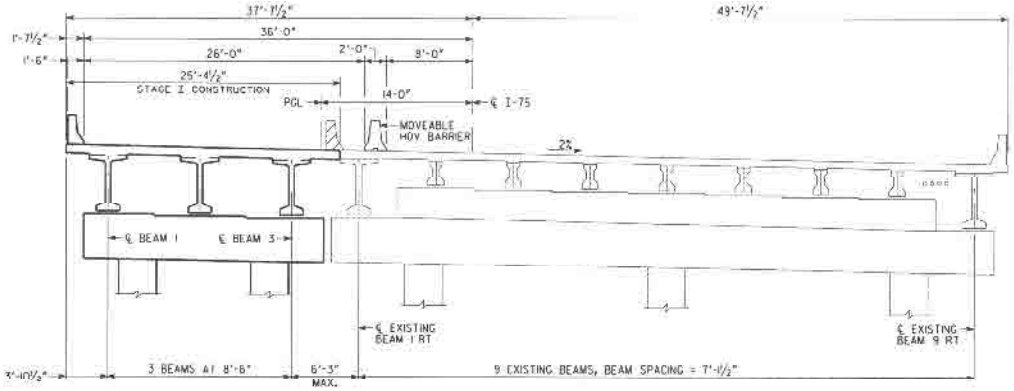

DECK SECTION
(LOOKING AHEAD, RIGHT BRIDGE)

CONSTRUCTION SEQUENCE

STAGE I:

1. PLACE TEMPORARY BARRIER, MAINTAIN THREE 12' O"LANES OF TRAFFIC IN EACH DIRECTION ON EXISTING BRIDGES. MAINTAIN EXIT LANE ON EXISTING NB BRIDGE.
2. REMOVE PORTIONS OF EXISTING NORTH BOUND BRIDGE AS NECESSARY FOR STAGE I CONSTRUCTION.
3. CONSTRUCT STAGE I SUBSTRUCTURE.
4. CONSTRUCT STAGE I SUPERSTRUCTURE.

NOTE !! IMPORTANT NOTICE! THIS DRAWING IS AN INCOMPLETE WORK-IN-PROGRESS AND ITS USE IS SUBJECT TO NOTE 1 ON DRAWING NO. 1-01.

BRIDGE NO. 32

DESIGN FILENAME—MICRO	11/20/09	
DRAWN BY	DATE	
CHECKED BY	DATE	
SUPERVISOR	DATE	
APPROVED	DATE	

REVISIONS

NO.	DATE	DESCRIPTION	DRG	CHKR	SUPV	APPR
A	2/10/02	Progress Drawings (1st Review)	AJM	JPS	GLB	SJL
B	4/25/03	50% SUBMISSION	AJM	JPS	GLB	SJL
C	10/10/03	PLOTTED PER SDDPTO TERMINATION FOR CONVENIENCE BIDDING	AJM			

GTP Georgia Transportation Partners

NORTHWEST I-75/I-575 CORRIDOR

DEPARTMENT OF TRANSPORTATION
STATE OF GEORGIA

JBT J.B. Trimble, Inc.
2550 Heritage Ct, SE Suite 250
Atlanta GA 30339-3062
(770) 952-1022

BRIDGE SHEET 2 OF 5

I-75 / I-575 NORTHWEST CORRIDOR

I-75 REVERSIBLE OVER BIG SHANTY CONN

CONSTRUCTION SEQUENCE

COBB COUNTY NH000-0073-03(242)

DRAWING NO. 35-204
